

4th May 2026.**MINUTES FOR SITE MEETING HELD ON 4th MAY 2026 FOR GARDEN DEVELOPMENT, MABUSHI, ABUJA FCT.**

Location: Mabushi
Project: Event Center at Plot 2030 Mabushi
Facilitator: Arc. Chike

Attendees:

1. Barr. Lanre
2. Arc. Chike
3. Engr. Kanabe
4. Surveyor
5. Ekene

ITEM	DESCRIPTION	ACTION
1	<u>Drainage:</u> The surveyor requested a plan for the drainage, particularly for the culvert, as the existing rings are undersized (see Fig. 1). Engr. Kanabe stated that he has been informed that the contract for the access road has been awarded. His intention is to wait for the road contractor to mobilize to site, as the cost of constructing a box culvert is significant. The surveyor advised that the size of the culvert rings should be increased as soon as possible to prevent future drainage issues. Arc. Chike recommended that work should commence on site, particularly in establishing levels. This will help reduce debris and litter currently obstruct the drainage path, allowing water to flow more freely. He added that by the time this is achieved, the road contractor may have mobilized, after which the replacement of the culvert rings can be properly considered.	Consultant Engineer

2	<u>Site Levels and Perimeter Wall:</u> The surveyors marked the DPC level and the grade level of the site (see Fig. 2). The marked level is nearly the same height as the existing perimeter wall at the entrance (see Fig. 3). The surveyor raised concerns about the load that the proposed filling may impose on the perimeter wall. In response, Engr. Kanabe stated that the perimeter walls are intended to be filled with weak concrete to improve their load bearing capacity.	Consultant Engineer
3	<u>Labour Agreement:</u> Engr. Kanabe stated that the client has an agreement with a group of labourers to excavate the retaining and perimeter wall base, with the work scheduled to be completed within two days.	

IMAGES



Fig. 1 Culvert with debris in water path

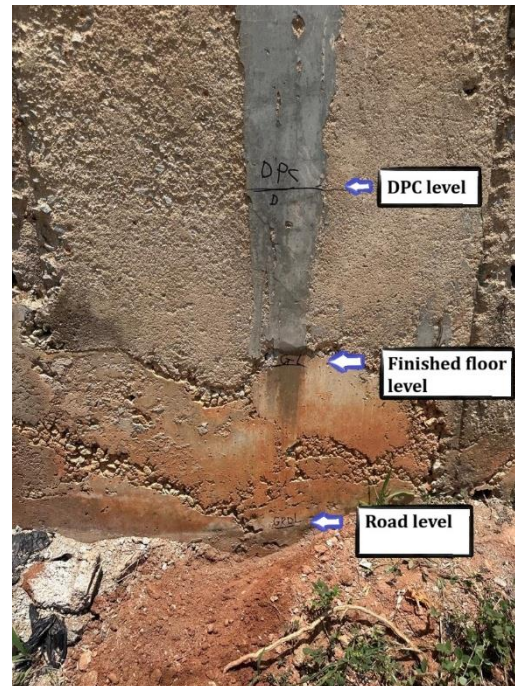


Fig. 2 Site levels as given by surveyor



Fig 3. Finished floor level

RECOMMENDATIONS

1. Changes to the Perimeter Wall

The height of the perimeter wall should be increased by a minimum of three courses above the currently proposed level and be made into a double wall. This adjustment is necessary to accommodate the anticipated final ground levels and to ensure adequate containment of the filled material within the site.

2. Commencement of Filling with Weak Concrete

It is recommended that filling works commence using weak concrete in the designated areas. This approach will allow for early progression of site filling operations without creating obstructions to subsequent works.

3. Construction of Perimeter Wall at Access Point

The perimeter wall should be commenced at the intended pedestrian access point into the site as a matter of priority. This will help secure the site boundary, control access, and reduce the risk of encroachment.

4. Drainage Clearance and Performance Assessment

All debris and litter within the existing drainage channel should be cleared immediately to restore free flow of water.

Following this, the drainage system should be observed under normal flow conditions to assess its performance. The decision to upgrade or redesign the culvert should be based on this assessment, alongside considerations of the proposed finished floor levels.

5. Monitoring of Excavation Labour and Contingency Plan

The labourers engaged for the excavation works should be closely monitored to ensure that progress aligns with the agreed schedule.

If the current workforce is unable to meet the required timeline, an alternative team be promptly engaged to carry out the excavation of the fence line. This will help prevent delays to subsequent activities and maintain overall project momentum.

For; Maccaferra



Arc. Chike Nnaobi
